Port of Seward Capacity and Resiliency Project - Preliminary Schedule

ID	Task Name	Duration	Start	Finish	Predecessors
1	**Grant Application/Notice of Award**	**0 wks**	**6/28/2026**	**6/28/2026**	
2	**Grant Award**	**56 wks**	**6/28/2026**	**7/22/2027**	
3	**Letter of Funding Commitment**	**4 wks**	**6/28/2026**	**7/23/2026**	**1**
4	**Project Grant Award**	**52 wks**	**7/24/2026**	**7/22/2027**	
5	Kick Off Meeting	2 wks	7/24/2026	8/6/2026	3
6	Site Visit	4 wks	8/7/2026	9/3/2026	5
7	**Engineering Risk Register**	**16 wks**	**9/4/2026**	**12/24/2026**	
8	DRAFT eRR	8 wks	9/4/2026	10/29/2026	6
9	Finalize eRR	8 wks	10/30/2026	12/24/2026	8
10	**Grant Agreement**	**46 wks**	**9/4/2026**	**7/22/2027**	
11	Grant Pre-Award Approval	4 wks	9/4/2026	10/1/2026	6
12	Draft Grant Agreement	12 wks	12/25/2026	3/18/2027	5,9
13	Grant Execution	6 wks	6/11/2027	7/22/2027	23,12
14	**Grant Implementation**	**142 wks**	**6/28/2026**	**3/15/2029**	
15	Grant Execution	0 wks	6/28/2026	6/28/2026	1
16	Grant Close out	8 wks	1/19/2029	3/15/2029	27
17	**Engineering Design**	**54 wks**	**10/2/2026**	**10/14/2027**	
18	Update 65% Design	4 wks	10/2/2026	10/29/2026	11
19	Design 85%	12 wks	10/30/2026	1/21/2027	18
20	Final PS&E	8 wks	7/23/2027	**9/16/2027**	19,13
21	**IFC complete**	**4 wks**	**9/17/2027**	**10/14/2027**	**20**
22	**Environmental**	**32 wks**	**10/30/2026**	**6/10/2027**	
23	**NEPA-Completion Confirmed**	**32 wks**	**10/30/2026**	**6/10/2027**	**5,18**
24	EA and FONSI if changes needed	32 wks	10/30/2026	6/10/2027	18,26FF
25	**Permits**	**12 wks**	**10/30/2026**	**1/21/2027**	
26	Mods to Corp Permit	12 wks	10/30/2026	1/21/2027	18
27	**Construction**	**66 wks**	**10/15/2027**	**1/18/2029**	
28	Contract Solicitation - NTP	12 wks	10/15/2027	1/6/2028	17
29	Materials	16 wks	1/7/2028	4/27/2028	28
30	Mobilization	2 wks	4/28/2028	5/11/2028	29
31	Mitigation	16 wks	5/12/2028	8/31/2028	30
32	Fill and Compact	16 wks	9/1/2028	12/21/2028	31
33	Substantial Complete	0 wks	12/21/2028	12/21/2028	32
34	Final Complete	4 wks	12/22/2028	1/18/2029	33

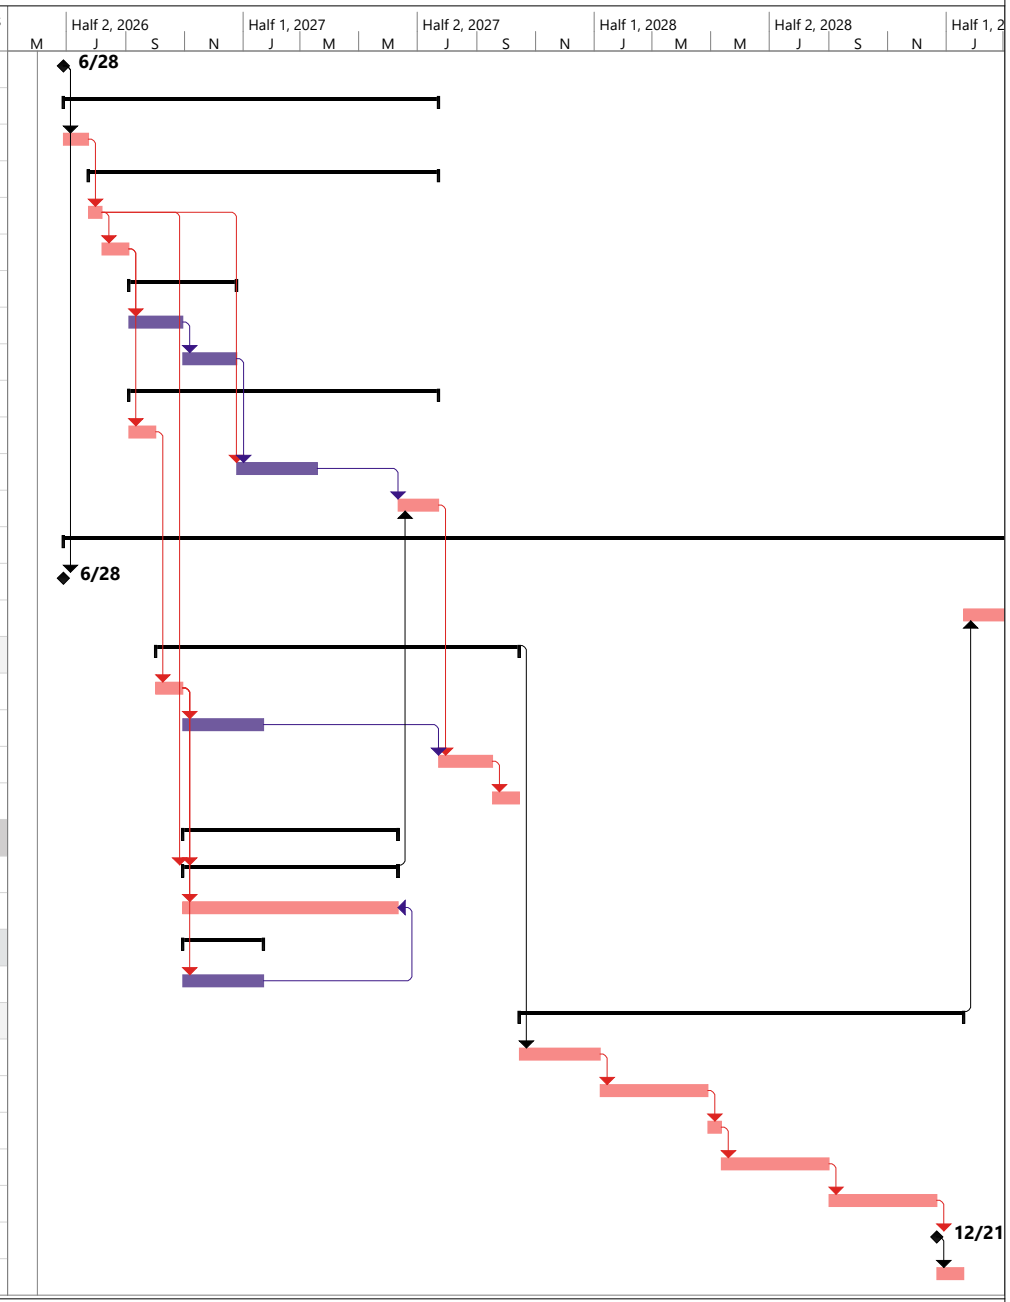

Project: Seward Freight Dock Ex
Date: 2/17/2026
File: SFD-Widening Grant R6.m

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress
