ARRC BRIDGE 127.5 PROJECT SCHEDULE

ID	Task Name	Duration	Start	Finish
0	**BR 227.1**	**372 days**	**Mon 6/17/24**	**Tue 6/24/25**
1	**BR 227.1**	**372 days**	**Mon 6/17/24**	**Tue 6/24/25**
2	**Pre-Construction**	**356 days**	**Mon 6/17/24**	**Sun 6/8/25**
3	**MOB Equipment**	**29 days**	**Mon 6/17/24**	**Tue 7/16/24**
4	Equipment to Seattle	10 days	Mon 6/17/24	Thu 6/27/24
5	Seattle to Whittier	14 days	Thu 6/27/24	Thu 7/11/24
6	Whittier to Talkeetna	5 days	Thu 7/11/24	Tue 7/16/24
7	**DEMOB Equipment**	**29 days**	**Sat 5/10/25**	**Sun 6/8/25**
8	Talkeetna to Whittier	5 days	Sat 5/10/25	Thu 5/15/25
9	Whittier to Seattle	14 days	Thu 5/15/25	Thu 5/29/25
10	Seattle to Yard	10 days	Thu 5/29/25	Sun 6/8/25
11	**Materials**	**90 days**	**Thu 6/27/24**	**Wed 9/25/24**
12	Bolts	21 days	Thu 6/27/24	Thu 7/18/24
13	Steel	90 days	Thu 6/27/24	Wed 9/25/24
14	Timber	21 days	Thu 6/27/24	Thu 7/18/24
15	**Construction**	**295 days**	**Fri 7/19/24**	**Sat 5/10/25**
16	Steel Prep	10 days	Fri 7/19/24	Mon 7/29/24
17	Rivet Removal and Temp Bolt Placement	21 days	Mon 7/29/24	Mon 8/19/24
18	Structual Steel and Permanent Bolt Placement	43 days	Mon 8/19/24	Tue 10/1/24
19	Trainmans Walk Replacement	31 days	Tue 10/1/24	Fri 11/1/24
20	Bearings and Bearing Pads	45 days	Sat 3/1/25	Tue 4/15/25
21	Tresspass Mitigation	14 days	Tue 4/15/25	Tue 4/29/25
22	Punch List	10 days	Tue 4/29/25	Fri 5/9/25
23	Final Walkthough	1 day	Fri 5/9/25	Sat 5/10/25
24	**Project Completion**	**56 days**	**Tue 4/29/25**	**Tue 6/24/25**
25	SUBSTANTIALLY COMPLETE	0 days	Tue 4/29/25	Tue 4/29/25
26	Final Closeout	56 days	Tue 4/29/25	Tue 6/24/25

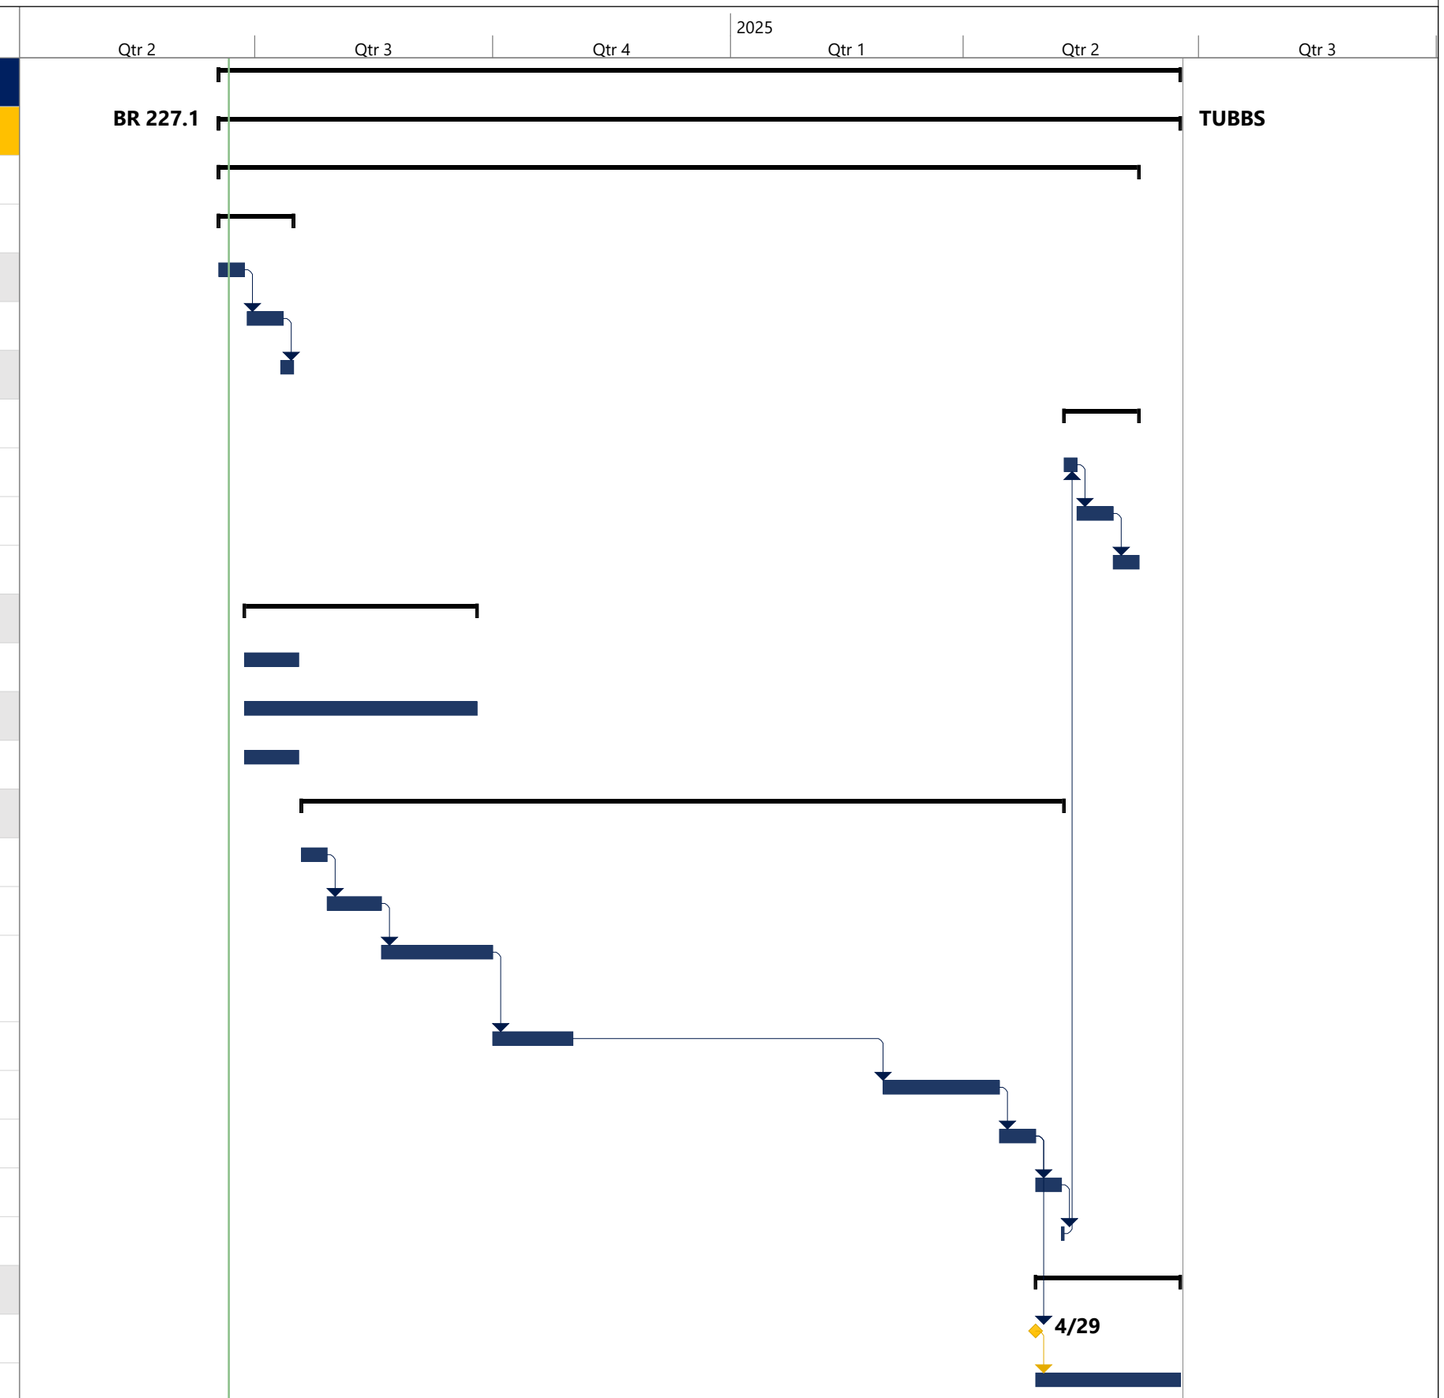

Project: BR 227.1
Date: Fri 6/21/24

Task | Milestone | Summary | Progress
